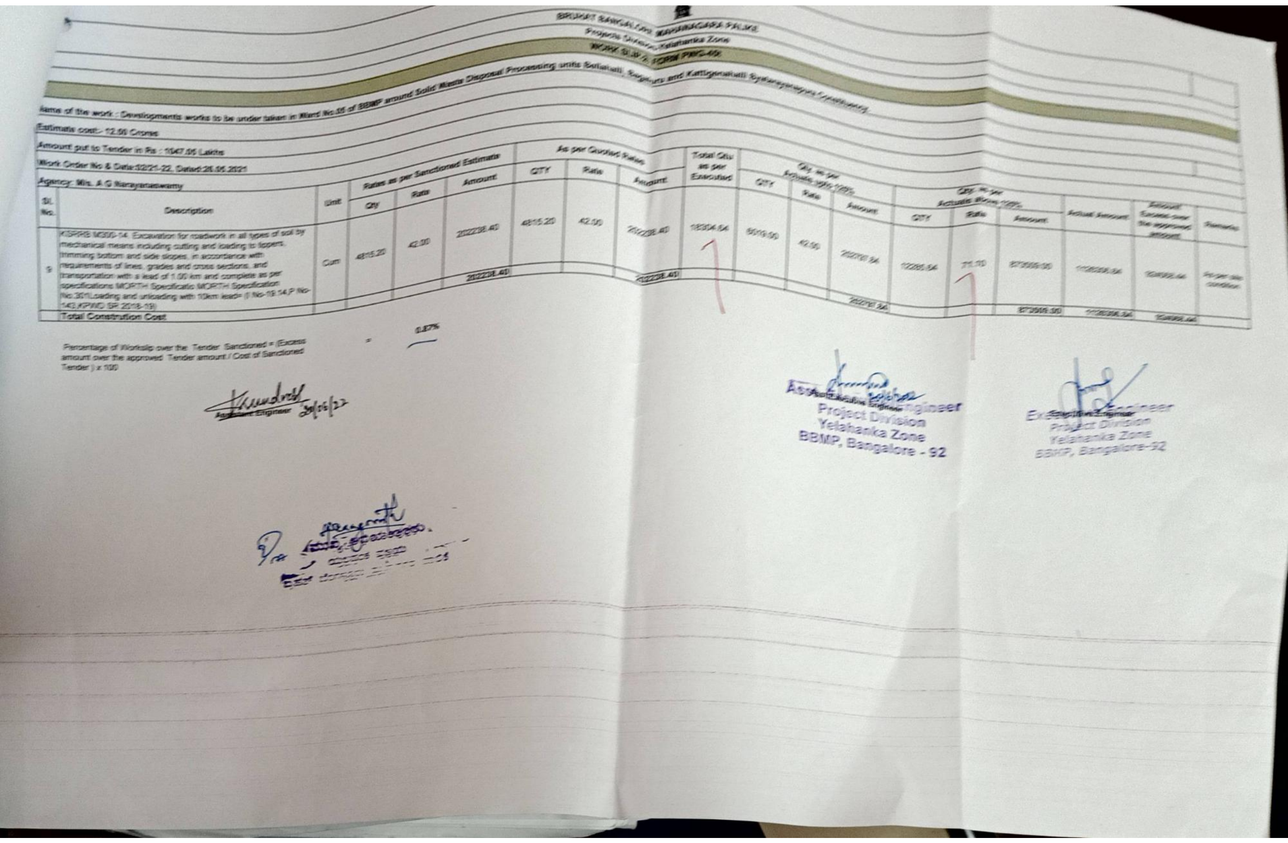

BRUHAT BANGALORE MAHANAGARA PALIKE
Projects Division, Yelahanka Zone
WORK SLIP & FORM PWD-45

Name of the work : Developments works to be under taken in Ward No.05 of BBMP around Solid Waste Disposal Processing units Bellahalli, Singanayakanahalli and Kattigenahalli Sydenahalli Constituency

Estimate cost:- 12.55 Crores

Amount put to Tender in Rs : 1547.05 Lakhs

Work Order No & Date:32/21-22, Dated:28.05.2021

Agency: M/s. A G Narayanaswamy

Sl. No.	Description	Unit	Rates as per Sanctioned Estimate			As per Gunfad Rates			Total Qty as per Executed	Qty as per Actuals upto 100%			Qty as per Actuals More 100%			Actual Amount	Amount Excess over the approved amount	Remarks
			Qty	Rate	Amount	QTY	Rate	Amount		QTY	Rate	Amount	QTY	Rate	Amount			
9	KSR'R/B:M:6/6-14, Excavation for roadwork in all types of soil by mechanical means including cutting and loading to lorpers, trimming bottom and side slopes, in accordance with requirements of lines, grades and cross sections, and transportation with a lead of 1.00 km and complete as per specifications MORTH Specification MORTH Specification No.301/Loading and unloading with 10km leadr (I No-19.14,P No-140,KPWD SP 2016-19)	Cum	4815.20	42.00	202238.40	4815.20	42.00	202238.40	19356.64	16016.00	42.00	672720.64	13285.64	71.70	952569.00	1625289.64	1504992.64	As per site condition
					202238.40			202238.40				672720.64			952569.00	1625289.64	1504992.64	
	Total Constrution Cost																	

Percentage of Worksip over the Tender Sanctioned = (Excess amount over the approved Tender amount / Cost of Sanctioned Tender) x 100 = 0.87%

Assistant Engineer
Project Division
Yelahanka Zone
BBMP, Bangalore - 92

Executive Engineer
Project Division
Yelahanka Zone
BBMP, Bangalore-92

Scanned by TapScanner
